WIPO Digital Access Service
Status update on the transition to ST.92 exchange

IP Office Business Solutions | November 2026

WIPO FOR OFFICIAL USE ONLY

Current status

- Validation of exchange workflows with non-hosted offices (USPTO and EPO) is in progress.
  - Patent workflow validation is complete.
  - Industrial design workflow validation is in progress and nearing completion.
- The next stage, starting in mid-November 2026, is to stress-test the WIPO DAS, USPTO and EPO endpoints by sending multiple parallel requests for the test samples, simulating DAS operation under peak demand.

WIPO
WORLD
INTELLECTUAL PROPERTY
ORGANIZATION

WIPO FOR OFFICIAL USE ONLY

ST.92 migration timeline

- Deployment of the WIPO DAS ST.92 services and the updated WIPO DAS Office Portal is planned for the weekend of 5–7 February 2027.
- Wave 1 will begin with USPTO and EPO migrating their current exchanges to priority document data packages (PDDPs). Final dates are still to be coordinated, but migration is expected in February 2027.
- Wave 1 will continue with testing and validation of the remaining Wave 1 offices between March and June 2027.
- Wave 2 offices are expected to migrate during 2027–2028.
- Status of offices moving to the ST.92 REST API:
  - Transition to ST.92 for offices directly connected to WIPO DAS (wiki)

WIPO
WORLD
INTELLECTUAL PROPERTY
ORGANIZATION

WIPO FOR OFFICIAL USE ONLY

Wave 1 offices (current list)

Office code	IP office	Type	Current connection	Wave	Time frame	Notes
CN	CNIPA	Non-hosted	TDA	1	May–June 2027	Test estimated for March-April 2027
EP	EPO	Non-hosted	TDA	1	Feb 2027	Stress tests starting mid-November 2026
KR	MOIP	Non-hosted	TDA	1	May–June 2027	Test estimated for March-April 2027
US	USPTO	Non-hosted	REST API V1	1	Feb 2027	Design workflow being validated; stress tests starting mid-November 2026
IB	WIPO	Hosted	REST API V1	1	Q1 2027	
NO	NIPO	Hosted	Office Portal	1 (TBC)	Feb 2027 (TBC)	Registration and retrieval through V2 being tested; should be ready for Wave 1

V1 / V2 = WIPO DAS REST API version 1 / version 2 (ST.92). TBC = to be confirmed.

WIPO
WORLD
INTELLECTUAL PROPERTY
ORGANIZATION

WIPO FOR OFFICIAL USE ONLY

Wave 2 offices (current list)

Office code	IP office	Type	Current connection	Wave	Time frame	Notes
AU	IP Australia	Hosted	REST API V1	2	2028	
DE	DPMA	Hosted	REST API V1	2 (TBC)	2027	DPMA setting up its V2 test environment
EM	EUIPO	Non-hosted	TDA	2 (TBC)	2027	V1 registration and status check in production; own endpoints and DAS retrieval from them pending; V2/PDDP testing and implementation planned for Q4 2026
ES	OEPM	Hosted	SFTP	2	2027	Planning stage
FR	INPI	Hosted	Office Portal (bulk)	2	2028	
GB	UKIPO	Hosted	SFTP	2	2027/2028	Registrations via V1; retrievals via a combination of SFTP and V1
IL	ILPO	Hosted	SFTP	2	2027	Project under way to move directly to V2
IS	IIPO	Hosted	Office Portal	2	2027/2028	
JP	JPO	Non-hosted	TDA	2	2028	Server connectivity and security assurance of REST API exchange under discussion
NZ	IPONZ	Hosted	SFTP	2	2028	Planning stage
SE	PRV	Hosted	SFTP	2	2027	Planning stage

V1 / V2 = WIPO DAS REST API version 1 / version 2 (ST.92). TBC = to be confirmed.

WIPO
WORLD
INTELLECTUAL PROPERTY
ORGANIZATION

WIPO FOR OFFICIAL USE ONLY

WIPO DAS Office Portal changes for ST.92


- As of November 2026, 43 offices exclusively use the WIPO DAS Office Portal.
- Two offices (AU and GB) occasionally use it to resolve urgent registration requests.
- Currently, only PDF files are exchanged via the Office Portal.
- This will change when the new DAS services go into production over the weekend of 5–7 February 2027.

WIPO
WORLD
INTELLECTUAL PROPERTY
ORGANIZATION

WIPO FOR OFFICIAL USE ONLY

Registration

- The user interface (UI) will change to help users build their own PDDP files:

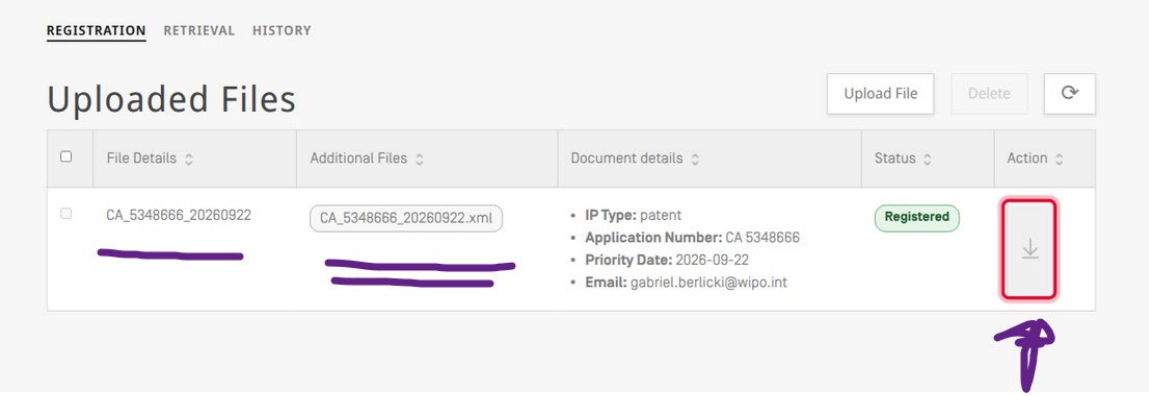

- Users will be able to attach further files submitted by the applicant to the application being registered, including ST.26 sequence listings (XML) and 3D drawings.
- Users will also be able to download the PDDP file generated by the UI before it is submitted to WIPO DAS.

WIPO
WORLD
INTELLECTUAL PROPERTY
ORGANIZATION


WIPO FOR OFFICIAL USE ONLY

Registration UI demo (video)

Video also available on the wiki: Registration request process for ST.92 files

WIPO
WORLD
INTELLECTUAL PROPERTY
ORGANIZATION

WIPO FOR OFFICIAL USE ONLY




WIPO
WORLD
INTELLECTUAL PROPERTY
ORGANIZATION

WIPO FOR OFFICIAL USE ONLY

Retrieval

- The user interface and retrieval steps remain unchanged.
- Only the downloaded file changes: under ST.92, the download link provides the PDDP package as a ZIP file instead of a PDF:

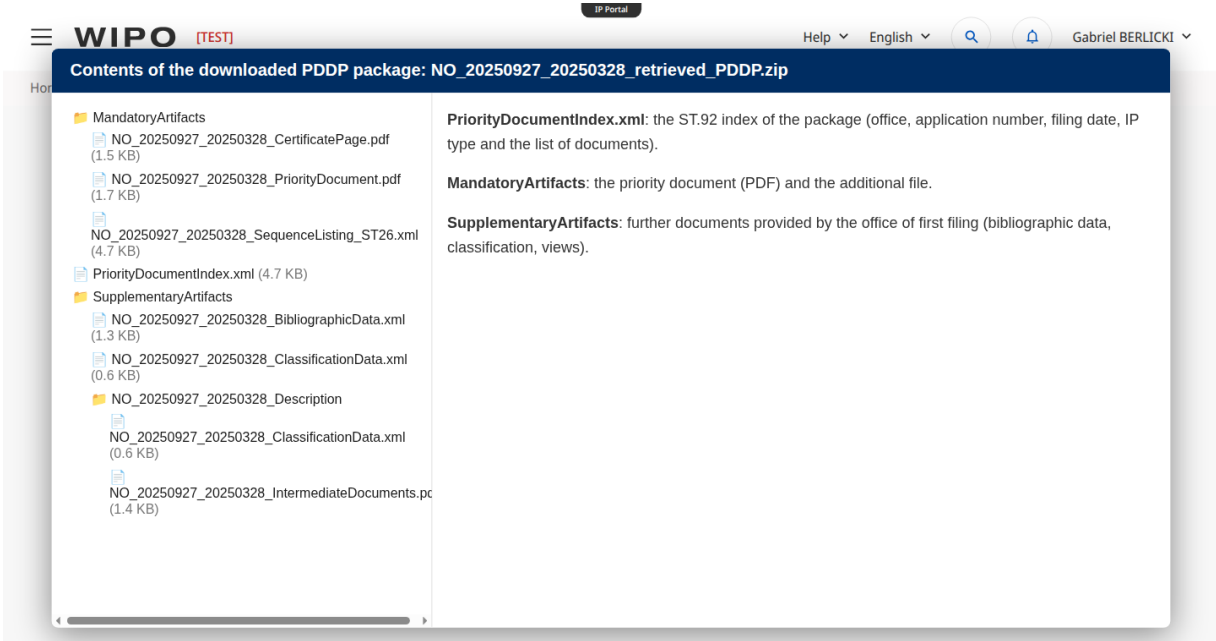


WIPO
WORLD
INTELLECTUAL PROPERTY
ORGANIZATION

Retrieval UI demo (video)

Video also available on the wiki: Retrieval request process for ST.92 files

WIPO
WORLD
INTELLECTUAL PROPERTY
ORGANIZATION

WIPO FOR OFFICIAL USE ONLY



WIPO
WORLD
INTELLECTUAL PROPERTY
ORGANIZATION

WIPO FOR OFFICIAL USE ONLY

Updated user guides

- New wiki pages document registration and retrieval in the WIPO DAS Office Portal step by step.
- In addition to screenshots, the pages include videos (including those shown in the demos) covering registration and retrieval of patents, designs and trademarks, with and without additional content.
- Wiki pages:
  - Registration request process for ST.92 files
  - Retrieval request process for ST.92 files

WIPO
WORLD
INTELLECTUAL PROPERTY
ORGANIZATION

WIPO FOR OFFICIAL USE ONLY

Next steps and key dates

Mid-November 2026	Stress tests of the WIPO DAS, USPTO and EPO endpoints begin
5–7 February 2027	Deployment of the WIPO DAS ST.92 services and the updated Office Portal
February 2027	USPTO and EPO migrate to PDDP exchange (final dates to be coordinated)
March–June 2027	Testing and validation of the remaining Wave 1 offices
July 1st 2027– June 30th 2028	Wave 2 office migrations

WIPO
WORLD
INTELLECTUAL PROPERTY
ORGANIZATION

WIPO FOR OFFICIAL USE ONLY
